


SCHEDULE F


BayCrossing

GENERAL EROSION CONTROL NOTES

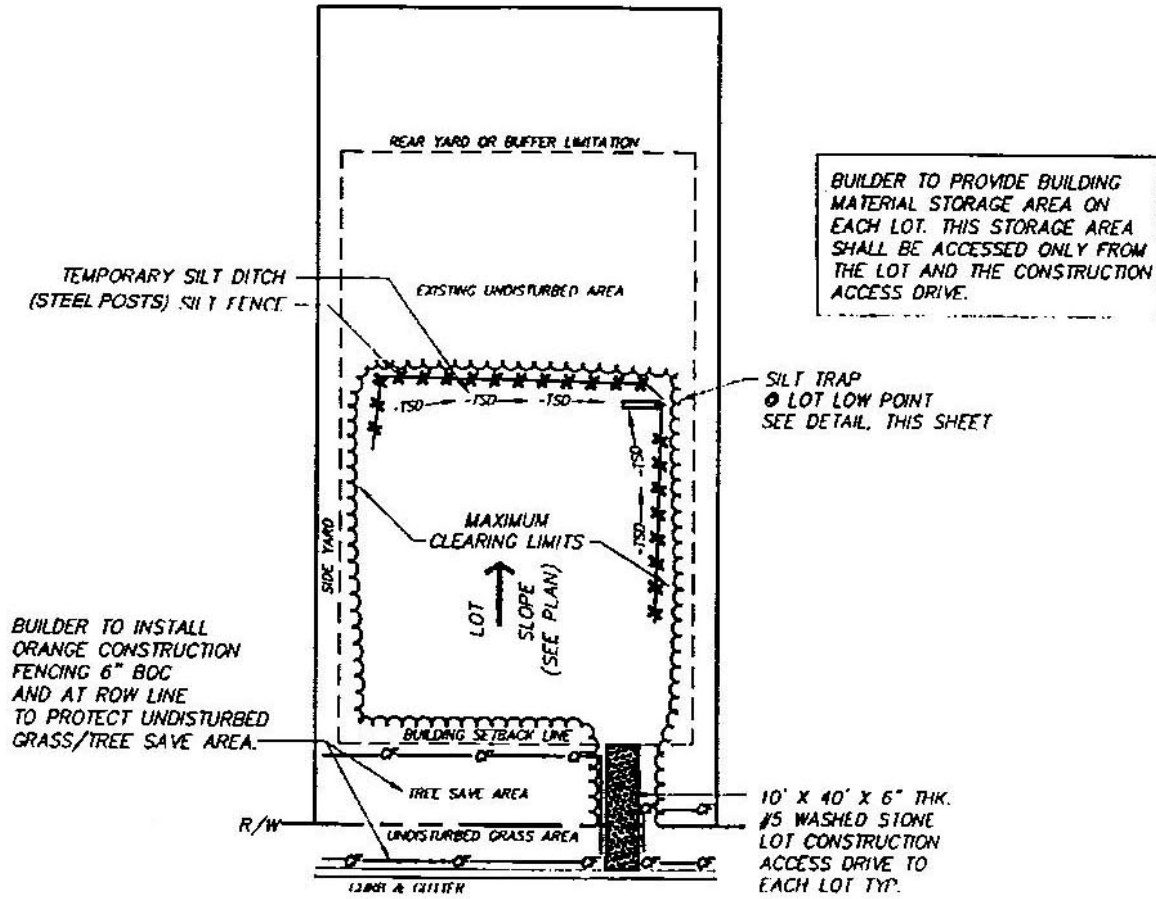


TYPICAL LOT DEVELOPMENT EROSION CONTROL

LOT SLOPING AWAY FROM STREET

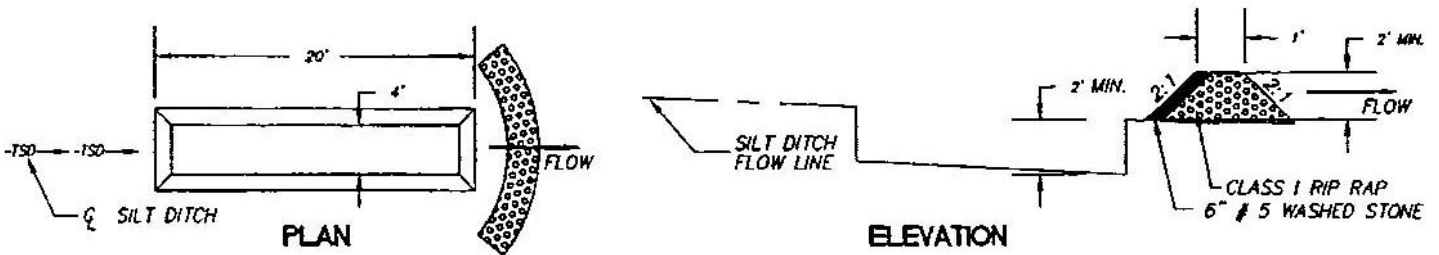

SILT TRAP DETAIL

BUILDER TO PROVIDE BUILDING MATERIAL STORAGE AREA ON EACH LOT. THIS STORAGE AREA SHALL BE ACCESSED ONLY FROM THE LOT AND THE CONSTRUCTION ACCESS DRIVE.


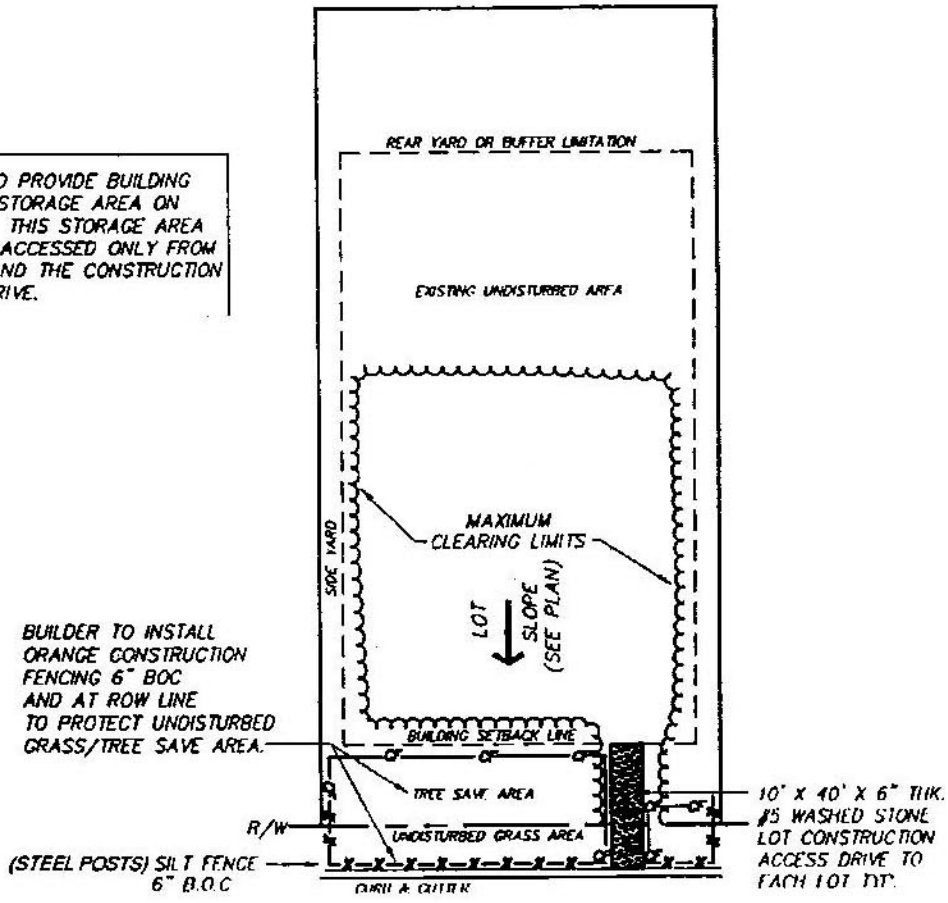


BUILDER TO INSTALL ORANGE CONSTRUCTION FENCING 6" BOC AND AT ROW LINE TO PROTECT UNDISTURBED GRASS/TREE SAVE AREA.

10' X 40' X 6" THK. #5 WASHED STONE LOT CONSTRUCTION ACCESS DRIVE TO EACH LOT TYP.

TYPICAL LOT DEVELOPMENT EROSION CONTROL

LOT SLOPING TOWARD STREET

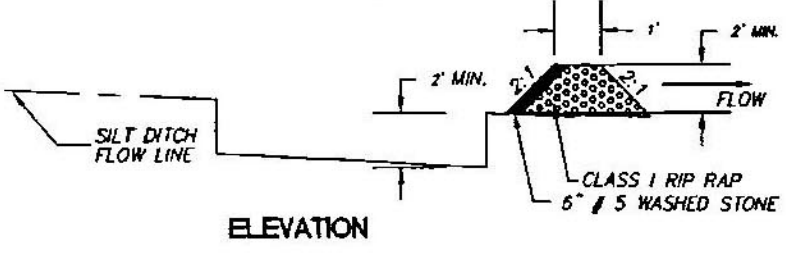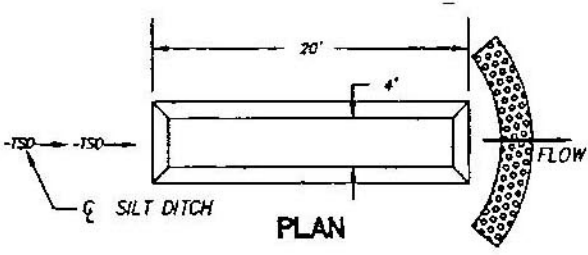

SILT TRAP DETAIL

1. Erosion control measures shall be provided for each lot as it is developed.
2. The owner shall be responsible for installing and maintaining the erosion control measures for each lot owned by such owner.
3. The owner shall install a #5 washed stone construction access to each lot owned by such owner. Access to each lot shall be via this drive only. The owner shall not encroach or allow any encroachment into the undisturbed grass area between the back of curb and the right-of-way line with materials or vehicles.
4. The owner shall provide a material storage area on each lot owned by such owner. This storage area shall be accessed only from the lot or the construction access drive.
  5. The typical lot erosion control measures shown shall be field located and adjusted to reflect the final grades and actual field conditions of each lot.
6. The owner shall provide maintenance inspections of all lot erosion control measures on a daily basis and after rainfall. Repairs shall be performed immediately.
7. The owner shall at all times remain cognizant of and in obedience with the restriction prohibiting clearing, grading or construction of any kind within the limits of the Lake Buffer Areas.
